


PROJECT:
CONSTRUCTION, COMPLETION AND MAINTENANCE OF
(20NOS) HOUSING UNITS AND MAINTENANCE OF
(32NOS) HOUSING UNITS AT HALANIYAT ISLAND IN
DHOFAH GOVERNORATE (TENDER NO : 213/2023)

CLIENT: MINISTRY OF HOUSING AND URBAN PLANNING
CONSULTANT: AL MANARAH ENGINEERING
CONSULTANCY
CONTRACTOR: EAST WATERFALLS TRADING &
CONTRACTING COMPANY

MOBILIZATION: 03 JUNE 2024 TO 30 SEPT. 2024
PROJECT DURATION: 730 Days
PROJECT COMMENCEMENT DATE: 01st Oct, 2024
PROJECT COMPLETION DATE: 30th Sep, 2026

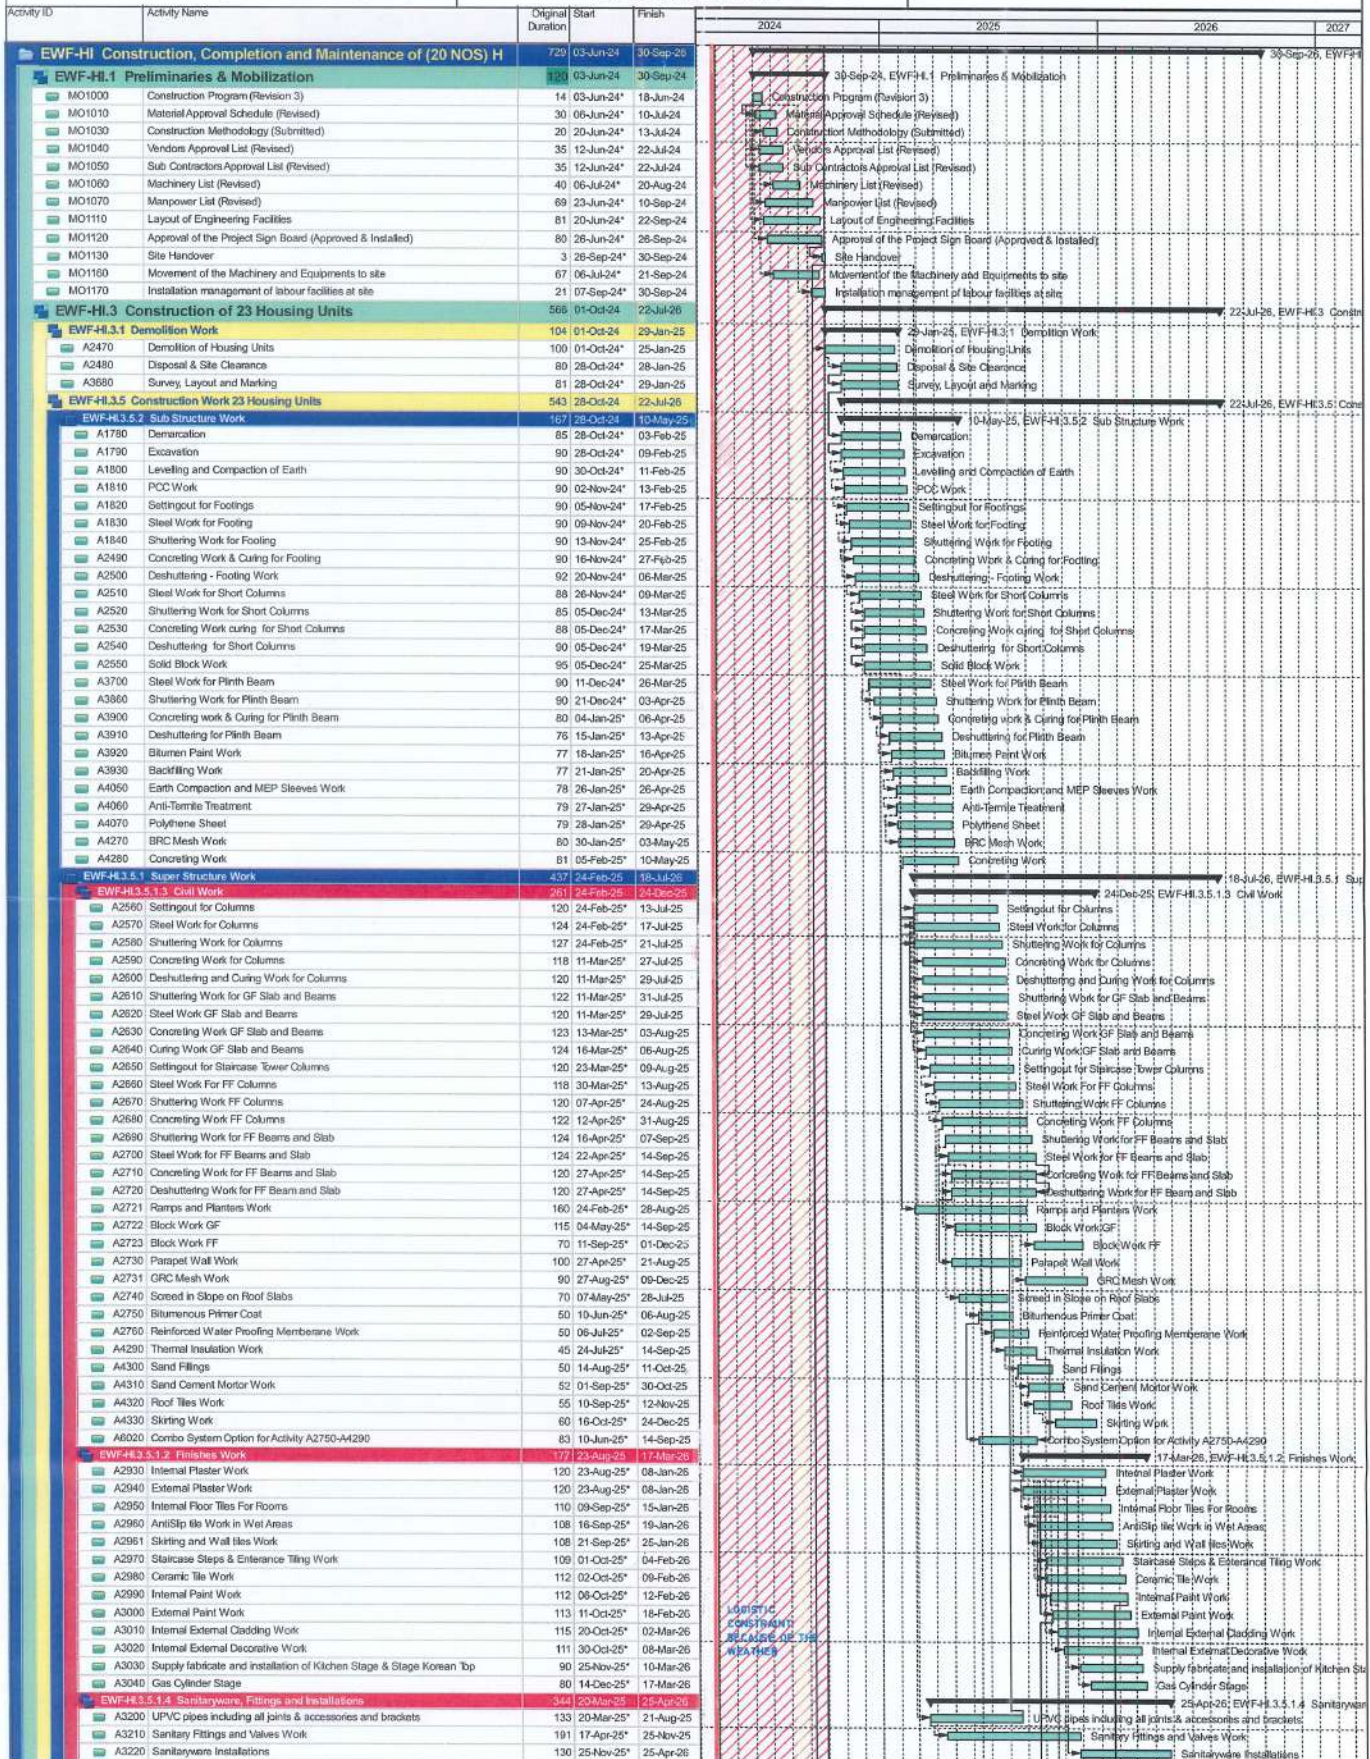

Actual Level of Effort Remaining Work
Actual Work Critical Remaining Work

Page 1 of 6

Eng. Muhammad Ahmed
muhammad.ahmed@eastwaterfalls.com


Approved as
general program.
Detail plan/schedule
to be shown on FORT night.



PROJECT:
CONSTRUCTION, COMPLETION AND MAINTENANCE OF
(20NOS) HOUSING UNITS AND MAINTENANCE OF
(32NOS) HOUSING UNITS AT HALANIYAT ISLAND IN
DHOFAH GOVERNORATE (TENDER NO : 213/2023)

CLIENT: MINISTRY OF HOUSING AND URBAN PLANNING
CONSULTANT: AL MANARAH ENGINEERING
CONSULTANCY
CONTRACTOR: EAST WATERFALLS TRADING &
CONTRACTING COMPANY

MOBILIZATION: 03 JUNE 2024 TO 30 SEPT. 2024
PROJECT DURATION: 730 Days
PROJECT COMMENCEMENT DATE: 01st Oct, 2024
PROJECT COMPLETION DATE: 30th Sep, 2026

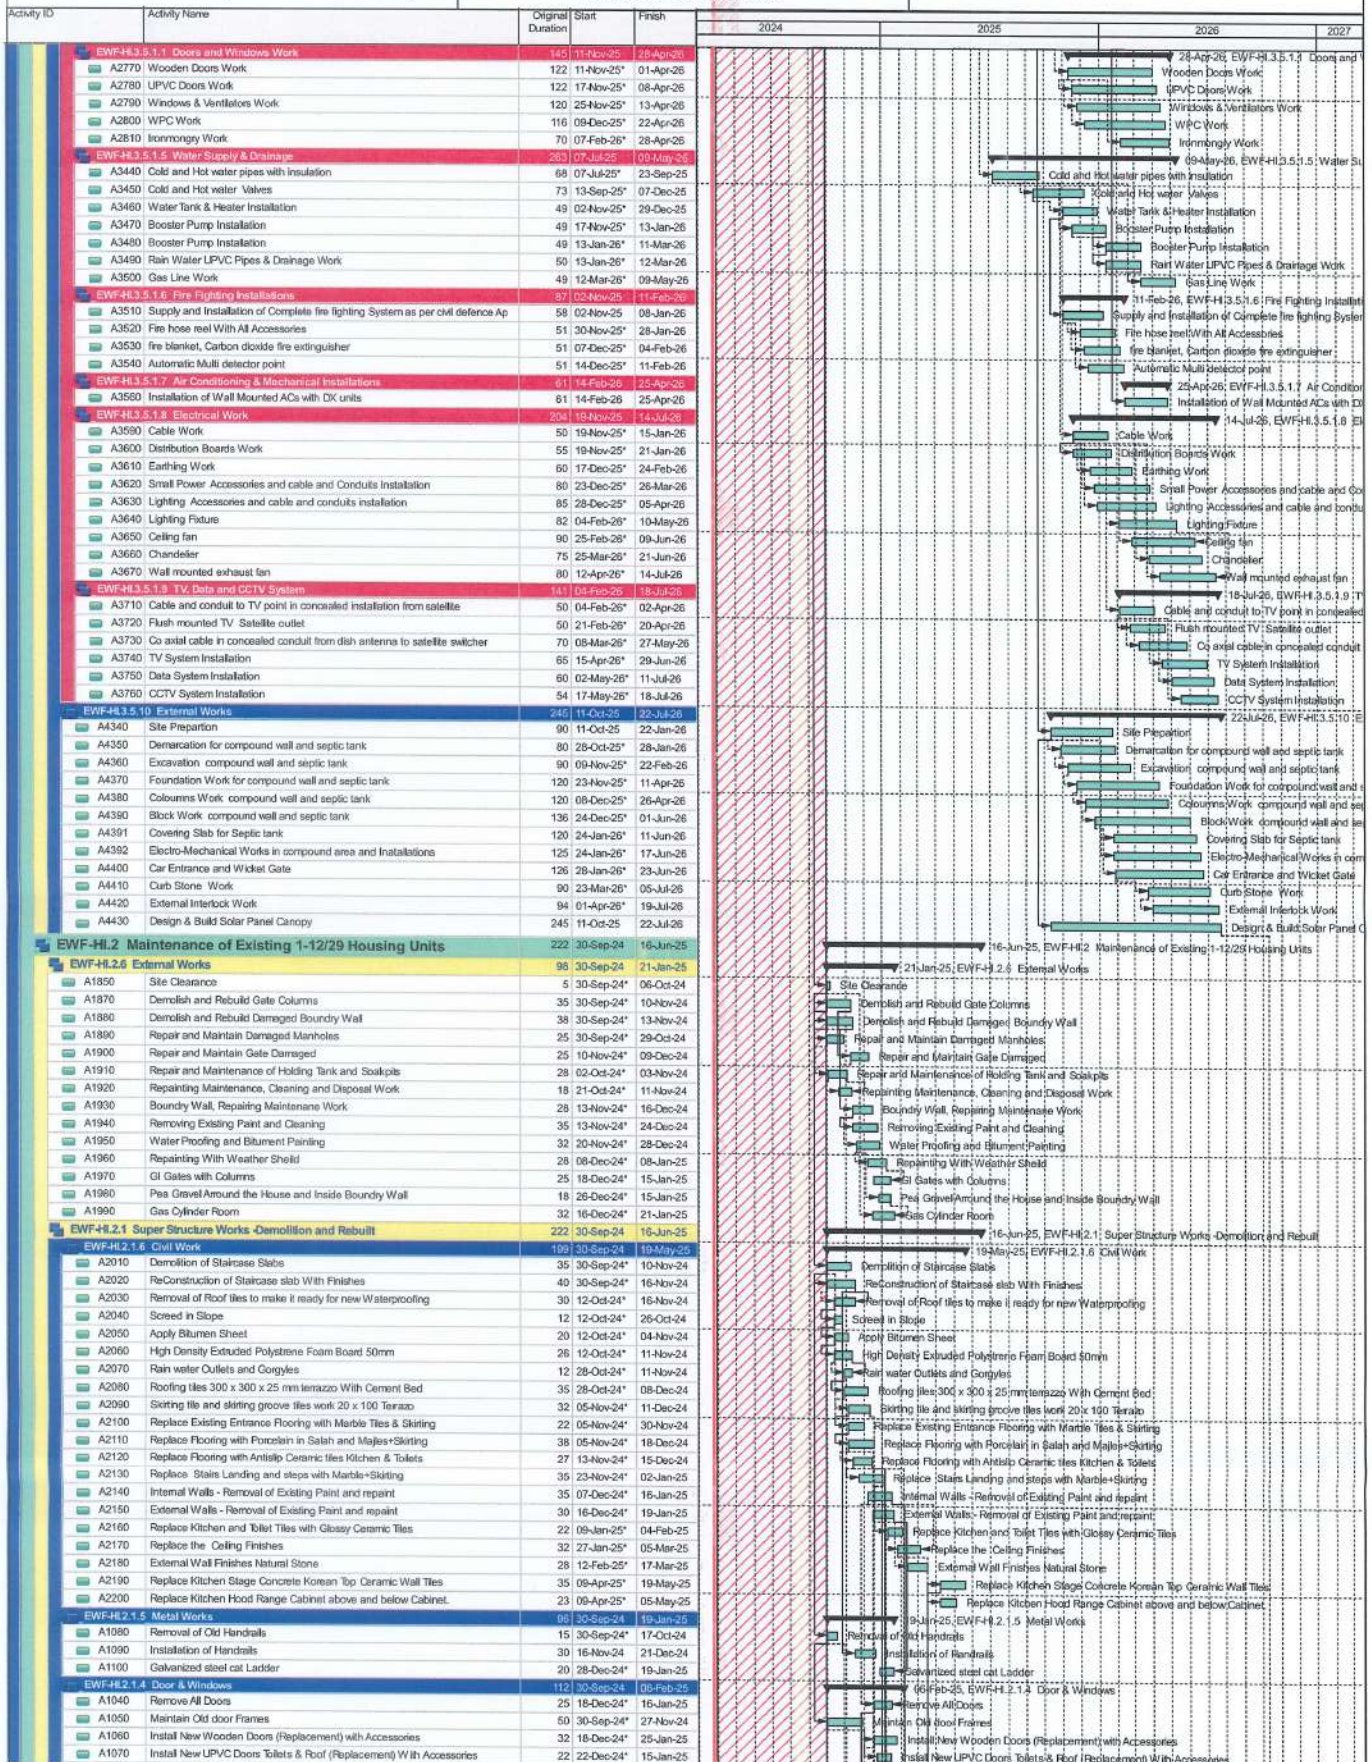

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work



PROJECT:
CONSTRUCTION, COMPLETION AND MAINTENANCE OF
(20NOS) HOUSING UNITS AND MAINTENANCE OF
(32NOS) HOUSING UNITS AT HALANIYAT ISLAND IN
DHOFAR GOVERNORATE (TENDER NO : 213/2023)

CLIENT: MINISTRY OF HOUSING AND URBAN PLANNING
CONSULTANT: AL MANARAH ENGINEERING
CONSULTANCY
CONTRACTOR: EAST WATERFALLS TRADING &
CONTRACTING COMPANY

MOBILIZATION: 03 JUNE 2024 TO 30 SEPT. 2024
PROJECT DURATION: 730 Days
PROJECT COMMENCEMENT DATE: 01st Oct, 2024
PROJECT COMPLETION DATE: 30th Sep, 2026

Activity ID	Activity Name	Original Duration	Start	Finish	2024	2025	2026	2027
A1110	Maintain Existing Aluminium Windows	69	19-Nov-24	06-Feb-25				
EWF-HL2.1.7	Sanitary Wares & Installations	167	03-Dec-24	16-Jun-25				
A1200	Remove all sanitary that were fixed	35	18-Dec-24	28-Jan-25				
A1210	Supply and Install Vent cowl	30	28-Jan-25	04-Mar-25				
A1220	Floor Drain trap	35	27-Feb-25	08-Apr-25				
A1230	Gully Trap	10	03-Dec-24	15-Dec-24				
A2210	Semi pedestal wash basin	10	28-Jan-25	09-Feb-25				
A2220	Stainless Steel Sink	10	09-Feb-25	20-Feb-25				
A2230	European Water Closet	10	20-Feb-25	04-Mar-25				
A2240	shower tray	12	04-Mar-25	18-Mar-25				
A2250	Abution Faucet	15	18-Mar-25	05-Apr-25				
A2260	shower Mixer	12	05-Apr-25	19-Apr-25				
A2270	Wash Basin Mixer	13	19-Apr-25	04-May-25				
A2280	Sink Mixer	12	04-May-25	18-May-25				
A2290	Toilet tissue holder	12	18-May-25	01-Jun-25				
A2300	Towel rail	12	01-Jun-25	15-Jun-25				
A2310	Mirror	13	01-Jun-25	16-Jun-25				
EWF-HL2.1.8	Water Supply & Rain Water Installations	107	21-Jun-25	25-May-26				
A1160	Pressure Test and Replace defects Polypropylene random copolymer pipe	30	21-Jun-25	24-Feb-26				
A1170	Cold and Hot water Valves	35	03-Feb-25	15-Mar-25				
A1180	Remove of all Equipment and Accessories that were fixed	30	18-Feb-25	24-Mar-25				
A1190	Water Tank Including Connection and Accessories	35	27-Feb-25	09-Apr-25				
A2380	Water Heater Connection and Accessories	35	06-Mar-25	16-Apr-25				
A2400	Rain Water LPVC Pipes with outlet	45	19-Mar-25	11-May-25				
A2410	Tap and Abution Faucet	31	20-Apr-25	25-May-25				
EWF-HL2.1.9	Electrical Installations	115	09-Jun-25	24-May-26				
A1120	Checking to Identify any issue in Existing Power Distribution System	5	11-Jan-25	16-Jan-25				
A1130	Installation of Solar system	116	09-Jun-25	24-May-26				
A1140	Replace the existing with new weatherproof IP 65 Main	15	16-Jan-25	03-Feb-25				
A1150	Small Power Accessories removing	10	03-Feb-25	15-Feb-25				
A2330	Small Power Accessories Installation	12	15-Feb-25	01-Mar-25				
A2340	Small Power Lighting Fixture removing	12	01-Mar-25	15-Mar-25				
A2350	Small Power Lighting Fixture Installations	12	15-Mar-25	29-Mar-25				
A2360	Ceiling Fan Installation with All Accessories	12	29-Mar-25	12-Apr-25				
A2370	Earthing Installations	12	12-Apr-25	26-Apr-25				
A2380	TV Points and Dish Installations	12	26-Apr-25	10-May-25				
EWF-HL2.1.10	Air Conditioning Work	55	06-Jan-25	11-Mar-26				
A1280	Remove all Equipments and Accessories Fixed Indoor/Outdoor	38	06-Jan-25	18-Feb-25				
A1290	Replace Wall mounted Split AC with DX unit	28	22-Jan-25	23-Feb-25				
A1300	Install Wall mounted Split AC with DX unit In Kitchen With Connections	25	30-Jan-25	27-Feb-25				
A1310	Install Wall mounted Split AC with DX unit in Salan & Majles	22	09-Feb-25	05-Mar-25				
A2320	Replace the Existing Ventilation Fans	20	17-Feb-25	11-Mar-25				
EWF-HL2.1.11	Partial Handing Over of 1-12/29 Units	60	17-Feb-25	27-Apr-25				
A4440	Handing over of Drawings	20	17-Feb-25	11-Mar-25				
A4450	Handing Over of Material Approvals	15	12-Mar-25	30-Mar-25				
A4460	Handing over of Warranty Guarantee Documents	10	30-Mar-25	10-Apr-25				
A4470	Handing Over of Inspection, Testing and Commissioning Reports	8	10-Apr-25	20-Apr-25				
A4480	Handing over of Keys	6	20-Apr-25	27-Apr-25				
A4490	Progress Report Compliance with Inventory and Sangelist	14	10-Apr-25	26-Apr-25				
EWF-HL.5	Maintenance of Existing 13-20/29 Housing Units	206	28-Apr-25	28-Dec-25				
EWF-HL5.6	External Works	80	28-Apr-25	29-Jul-25				
A4730	Site Clearance	5	28-Apr-25	03-May-25				
A4740	Demolish and Rebuild Gate Columns	31	03-May-25	08-Jun-25				
A4750	Demolish and Rebuild Damaged Boundry Wall	33	06-May-25	12-Jun-25				
A4760	Repair and Maintain Damaged Manholes	21	26-May-25	19-Jun-25				
A4770	Repair and Maintain Gate Damaged	22	08-Jun-25	03-Jul-25				
A4780	Repair and Maintenance of Holding Tank and Soakpits	25	19-Jun-25	19-Jul-25				
A4790	Repainting Maintenance, Cleaning and Disposal Work	15	01-Jul-25	19-Jul-25				
A4800	Boundry Wall, Repainting Maintenance Work	24	23-Jun-25	20-Jul-25				
A4810	Removing Existing Paint and Cleaning	30	25-Jun-25	29-Jul-25				
A4820	Water Proofing and Blument Painting	23	23-Jun-25	19-Jul-25				
A4830	Repainting With Weather Shield	25	26-Jun-25	24-Jul-25				
A4840	GI Gates with Columns	22	30-Jun-25	24-Jul-25				
A4850	Pea Gravel Around the House and Inside Boundry Wall	16	08-Jul-25	28-Jul-25				
A4860	Gas Cylinder Room	27	26-Jun-25	28-Jul-25				
EWF-HL5.1	Super Structure Works-Demolition and Rebuild	208	28-Apr-25	23-Dec-25				
EWF-HL5.1.6	Civil Work	157	28-Apr-25	27-Oct-25				
A4870	Demolition of Staircase Slabs	35	28-Apr-25	07-Jun-25				
A4880	ReConstruction of Staircase slab With Finishes	40	01-May-25	16-Jun-25				
A4890	Removal of Roof tiles to make it ready for new Waterproofing	30	15-May-25	18-Jun-25				
A4900	Screed in Slope	12	07-Jun-25	19-Jun-25				
A4910	Apply Bitumen Sheet	20	07-Jun-25	29-Jun-25				
A4920	High Density Extruded Polystyrene Foam Board 50mm	26	07-Jun-25	06-Jul-25				
A4930	Rain water Outlets and Gorgyles	12	23-Jun-25	06-Jul-25				
A4940	Roofing tiles 300 x 300 x 25 mm terrazzo With Cement Bed	35	23-Jun-25	02-Aug-25				
A4950	Skirting tile and skirting groove tiles work 20 x 100 Terrazo	32	23-Jun-25	04-Aug-25				
A4960	Replace Existing Entrance Flooring with Marble Tiles & Skirting	22	29-Jun-25	23-Jul-25				
A4970	Replace Flooring with Porcelain in Salan & Majles+Skirting	38	13-Jul-25	25-Aug-25				
A4980	Replace Flooring with Antislip Ceramic tiles Kitchen & Toilets	27	30-Jul-25	31-Aug-25				
A4990	Replace Stairs Landing and steps with Marble+Skirting	35	30-Jul-25	09-Sep-25				
A5000	Internal Walls - Removal of Existing Paint and repaint	35	30-Jul-25	09-Sep-25				
A5010	External Walls - Removal of Existing Paint and repaint	30	30-Jul-25	03-Sep-25				
A5020	Replace Kitchen and Toilet Tiles with Glossy Ceramic Tiles	22	09-Sep-25	05-Oct-25				
A5030	Replace the Ceiling Finishes	32	09-Sep-25	16-Oct-25				
A5040	External Wall Finishes Natural Stone	28	30-Jul-25	01-Sep-25				
A5050	Replace Kitchen Slag Concrete Korean Top Ceramic Wall Tiles	35	09-Sep-25	20-Oct-25				
A5060	Replace Kitchen Hood Range Cabinet above and below Cabinet.	23	30-Sep-25	27-Oct-25				
EWF-HL5.1.5	Metal Works	111	28-Apr-25	03-Sep-25				
A4540	Removal of Old Handrails	13	28-Apr-25	12-May-25				
A4550	Installation of Handrails	25	17-Jun-25	15-Jul-25				
A4560	Galvanized steel cat Ladder	17	14-Aug-25	03-Sep-25				
EWF-HL5.1.4	Door & Windows	87	12-Jun-25	21-Sep-25				
A4500	Remove All Doors	25	11-Aug-25	09-Sep-25				
A4510	Maintain Old door Frames	50	12-Jun-25	09-Aug-25				
A4520	Install New Wooden Doors (Replacement) with Accessories	32	11-Aug-25	17-Sep-25				
A4530	Install New UPVC Doors Toilets & Roof (Replacement) With Accessories	22	11-Aug-25	06-Sep-25				
A5280	Maintain Existing Aluminium Windows	69	03-Jul-25	21-Sep-25				
EWF-HL5.1.7	Sanitary Wares & Installations	120	30-Jul-25	17-Dec-25				

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work



PROJECT:
CONSTRUCTION, COMPLETION AND MAINTENANCE OF
(20NOS) HOUSING UNITS AND MAINTENANCE OF
(32NOS) HOUSING UNITS AT HALANIYAT ISLAND IN
DHOFAH GOVERNORATE (TENDER NO : 213/2023)

CLIENT: MINISTRY OF HOUSING AND URBAN PLANNING
CONSULTANT: AL MANARAH ENGINEERING
CONSULTANCY
CONTRACTOR: EAST WATERFALLS TRADING &
CONTRACTING COMPANY

MOBILIZATION: 03 JUNE 2024 TO 30 SEPT. 2024
PROJECT DURATION: 730 Days
PROJECT COMMENCEMENT DATE: 01st Oct, 2024
PROJECT COMPLETION DATE: 30th Sep, 2026

Activity ID	Activity Name	Original Duration	Start	Finish	2024	2025	2026	2027
A4650	Remove all sanitary that were fixed	28	11-Aug-25	13-Sep-25				
A4660	Supply and install Vent cowl	21	13-Sep-25	07-Oct-25				
A4670	Floor Drain trap	23	30-Jul-25	28-Aug-25				
A4680	Gully Trap	8	21-Aug-25	31-Aug-25				
A5070	Semi pedestal wash basin	8	13-Sep-25	22-Sep-25				
A5080	Stainless Steel Sink	7	22-Sep-25	30-Sep-25				
A5090	European Water Closet	8	30-Sep-25	09-Oct-25				
A5100	shower tray	7	09-Oct-25	18-Oct-25				
A5110	Ablution Faucet	9	18-Oct-25	28-Oct-25				
A5120	shower Mixer	9	28-Oct-25	08-Nov-25				
A5130	Wash Basin Mixer	9	08-Nov-25	18-Nov-25				
A5140	Sink Mixer	9	18-Nov-25	29-Nov-25				
A5160	Toilet tissue holder	8	29-Nov-25	08-Dec-25				
A5160	Towel rail	7	08-Dec-25	16-Dec-25				
A5170	Mirror	8	08-Dec-25	17-Dec-25				
EWF-HL.5.1.8	Water Supply & Rain Water Installations	56	31-Aug-25	04-Nov-25				
A4610	Pressure Test and Replace defects/Polypropylene random copolymer pipe	30	31-Aug-25	05-Oct-25				
A4620	Cold and Hot water Valves	35	03-Sep-25	14-Oct-25				
A4630	Remove of all Equipment and Accessories that were fixed	30	14-Sep-25	19-Oct-25				
A4640	Water Tank Including Connection and Accessories	35	10-Sep-25	21-Oct-25				
A5250	Water Heater Connection and Accessories	35	17-Sep-25	28-Oct-25				
A5260	Rain Water UPVC Pipes with outlet	45	10-Sep-25	02-Nov-25				
A5270	Tap and Ablution Faucet	31	29-Sep-25	04-Nov-25				
EWF-HL.5.1.9	Electrical Installations	118	05-Aug-25	17-Dec-25				
A4570	Checking to identify any issue in Existing Power Distribution System	5	03-Sep-25	09-Sep-25				
A4580	Installation of Solar system	90	05-Aug-25	17-Nov-25				
A4590	Replace the existing with new weatherproof IP 65 Main	15	09-Sep-25	27-Sep-25				
A4600	Small Power Accessories removing	10	27-Sep-25	08-Oct-25				
A5190	Small Power Accessories Installation	10	08-Oct-25	20-Oct-25				
A5200	Small Power Lighting Fixture removing	11	20-Oct-25	02-Nov-25				
A5210	Small Power Lighting Fixture Installations	9	02-Nov-25	12-Nov-25				
A5220	Ceiling Fan Installation with All Accessories	11	12-Nov-25	25-Nov-25				
A5230	Earthing Installations	10	25-Nov-25	07-Dec-25				
A5240	TV Points and Dish Installations	9	07-Dec-25	17-Dec-25				
EWF-HL.5.1.10	Air Conditioning Work	68	27-Aug-25	15-Nov-25				
A4690	Remove all Equipments and Accessories Fixed Indoor/Outdoor	32	27-Aug-25	04-Oct-25				
A4700	Replace Wall mounted Split AC with DX unit	23	14-Sep-25	09-Oct-25				
A4710	Install Wall mounted Split AC with DX unit In Kitchen With Connections	19	28-Sep-25	19-Oct-25				
A4720	Install Wall mounted Split AC with DX unit in Salah & Majles	18	15-Oct-25	04-Nov-25				
A5180	Replace the Existing Ventilation Fans	17	26-Oct-25	15-Nov-25				
EWF-HL.5.1.11	Partial Handing Over of 13-20/29 Units	67	07-Oct-25	23-Dec-25				
A5290	Handingover of Drawings	20	07-Oct-25	29-Oct-25				
A5300	Handing Over of Material Approvals	15	08-Nov-25	24-Nov-25				
A5310	Handing over of Warranty Guarantee Documents	10	25-Nov-25	06-Dec-25				
A5320	Handing Over of Inspection, Testing and Commissioning Reports	8	07-Dec-25	15-Dec-25				
A5330	Handingover of Keys	7	16-Dec-25	23-Dec-25				
A5340	Progress Report Compliance with Inventory and Sanglist	14	07-Dec-25	22-Dec-25				
EWF-HL.8	Maintenance of Existing 21-29/29 Housing Units	188	24-Dec-25	21-Jul-26				
EWF-HL.8.6	External Works	75	24-Dec-25	22-Mar-26				
A5580	Site Clearance	4	24-Dec-25	28-Dec-25				
A5590	Demolish and Rebuild Gate Columns	29	29-Dec-25	31-Jan-26				
A5600	Demolish and Rebuild Damaged Boundary Wall	31	01-Jan-26	05-Feb-26				
A5610	Repair and Maintain Damaged Manholes	20	12-Jan-26	03-Feb-26				
A5620	Repair and Maintain Gate Damaged	20	01-Feb-26	23-Feb-26				
A5630	Repair and Maintenance of Holding Tank and Slop pits	22	25-Jan-26	19-Feb-26				
A5640	Repainting Maintenance, Cleaning and Disposal Work	13	04-Feb-26	19-Feb-26				
A5650	Boundary Wall, Repainting Maintenance Work	22	07-Feb-26	03-Mar-26				
A5660	Removing Existing Paint and Cleaning	27	12-Feb-26	15-Mar-26				
A5670	Water Proofing and Bitumen Painting	21	21-Feb-26	17-Mar-26				
A5680	Repainting With Weather Shield	23	24-Feb-26	22-Mar-26				
A5690	GI Gates with Columns	30	14-Feb-26	19-Mar-26				
A5700	Pea Gravel Around the House and Inside Boundary Wall	15	24-Feb-26	14-Mar-26				
A5710	Gas Cylinder Room	24	21-Feb-26	21-Mar-26				
EWF-HL.8.1	Super Structure Works-Demolition and Rebuild	172	03-Jan-26	21-Jul-26				
EWF-HL.8.1.6	Civil Work	104	03-Jan-26	03-May-26				
A5720	Demolition of Staircase Slabs	32	03-Jan-26	08-Feb-26				
A5730	ReConstruction of Staircase slab With Finishes	35	08-Jan-26	17-Feb-26				
A5740	Removal of Roof tiles to make it ready for new Waterproofing	34	10-Jan-26	17-Feb-26				
A5750	Screed in Slope	31	17-Jan-26	21-Feb-26				
A5760	Apply Bitumen Sheet	18	04-Feb-26	24-Feb-26				
A5770	High Density Extruded Polystyrene Foam Board 50mm	24	04-Feb-26	03-Mar-26				
A5780	Rain water Outlets and Gorgies	11	19-Feb-26	03-Mar-26				
A5790	Roofing tiles 300 x 300 x 25 mm terrazzo With Cement Bed	31	19-Feb-26	26-Mar-26				
A5800	Skirting tile and skirting groove tiles work 20 x 100 Terrazo	30	23-Feb-26	29-Mar-26				
A5810	Replace Existing Entrance Flooring with Marble Tiles & Skirting	20	25-Feb-26	19-Mar-26				
A5820	Replace Flooring with Porcelain in Salah and Majles+Skirting	34	26-Feb-26	06-Apr-26				
A5830	Replace Flooring with Porcelain Kitchen & Toilets	24	04-Mar-26	28-Mar-26				
A5840	Replace Stairs Landing and steps with Marble+Skirting	30	05-Mar-26	08-Apr-26				
A5850	Internal Walls - Removal of Existing Paint and repaint	31	08-Mar-26	13-Apr-26				
A5860	External Walls - Removal of Existing Paint and repaint	27	14-Mar-26	13-Apr-26				
A5870	Replace Kitchen and Toilet Tiles with Glossy Ceramic Tiles	21	09-Apr-26	03-May-26				
A5880	Replace the Ceiling Finishes	25	16-Mar-26	13-Apr-26				
A5890	External Wall Finishes Natural Stone	25	15-Mar-26	12-Apr-26				
A5900	Replace Kitchen Stage Concrete Korean Top Ceramic Wall Tiles	31	29-Mar-26	03-May-26				
A5910	Replace Kitchen Hood Range Cabinet above and below Cabinet	21	09-Apr-26	03-May-26				
EWF-HL.8.1.5	Metal Works	83	31-Jan-26	13-Apr-26				
A5390	Removal of Old Handrails	12	31-Jan-26	12-Feb-26				
A5400	Installation of Handrails	23	18-Feb-26	16-Mar-26				
A5410	Galvanized steel cat Ladder	16	28-Mar-26	13-Apr-26				
EWF-HL.8.1.4	Door & Windows	69	31-Jan-26	20-Apr-26				
A5350	Remove All Doors	23	18-Mar-26	13-Apr-26				
A5360	Maintain Old door Frames	35	31-Jan-26	11-Mar-26				
A5370	Install New Wooden Doors (Replacement) with Accessories	29	18-Mar-26	20-Apr-26				
A5380	Install New UPVC Doors Toilets & Roof (Replacement) With Accessories	19	18-Mar-26	08-Apr-26				
A5130	Maintain Existing Aluminium Windows	40	31-Jan-26	17-Mar-26				
EWF-HL.8.1.7	Sanitary Wares & Installations	121	01-Mar-26	19-Jul-26				
A5500	Remove all sanitary that were fixed	28	18-Mar-26	19-Apr-26				
A5510	Supply and install Vent cowl	21	20-Apr-26	13-May-26				

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work

Page 4 of 6


Eng. Muhammad Ahmed
muhammed.ahmed@eastwaterfalls.com



PROJECT:
CONSTRUCTION, COMPLETION AND MAINTENANCE OF
(20NOS) HOUSING UNITS AND MAINTENANCE OF
(32NOS) HOUSING UNITS AT HALANIYAT ISLAND IN
DHOFAR GOVERNORATE (TENDER NO : 213/2023)

CLIENT: MINISTRY OF HOUSING AND URBAN PLANNING
CONSULTANT: AL MANARAH ENGINEERING
CONSULTANCY
CONTRACTOR: EAST WATERFALLS TRADING &
CONTRACTING COMPANY

MOBILIZATION: 03 JUNE 2024 TO 30 SEPT. 2024
PROJECT DURATION: 730 Days
PROJECT COMMENCEMENT DATE: 01st Oct, 2024
PROJECT COMPLETION DATE: 30th Sep, 2026

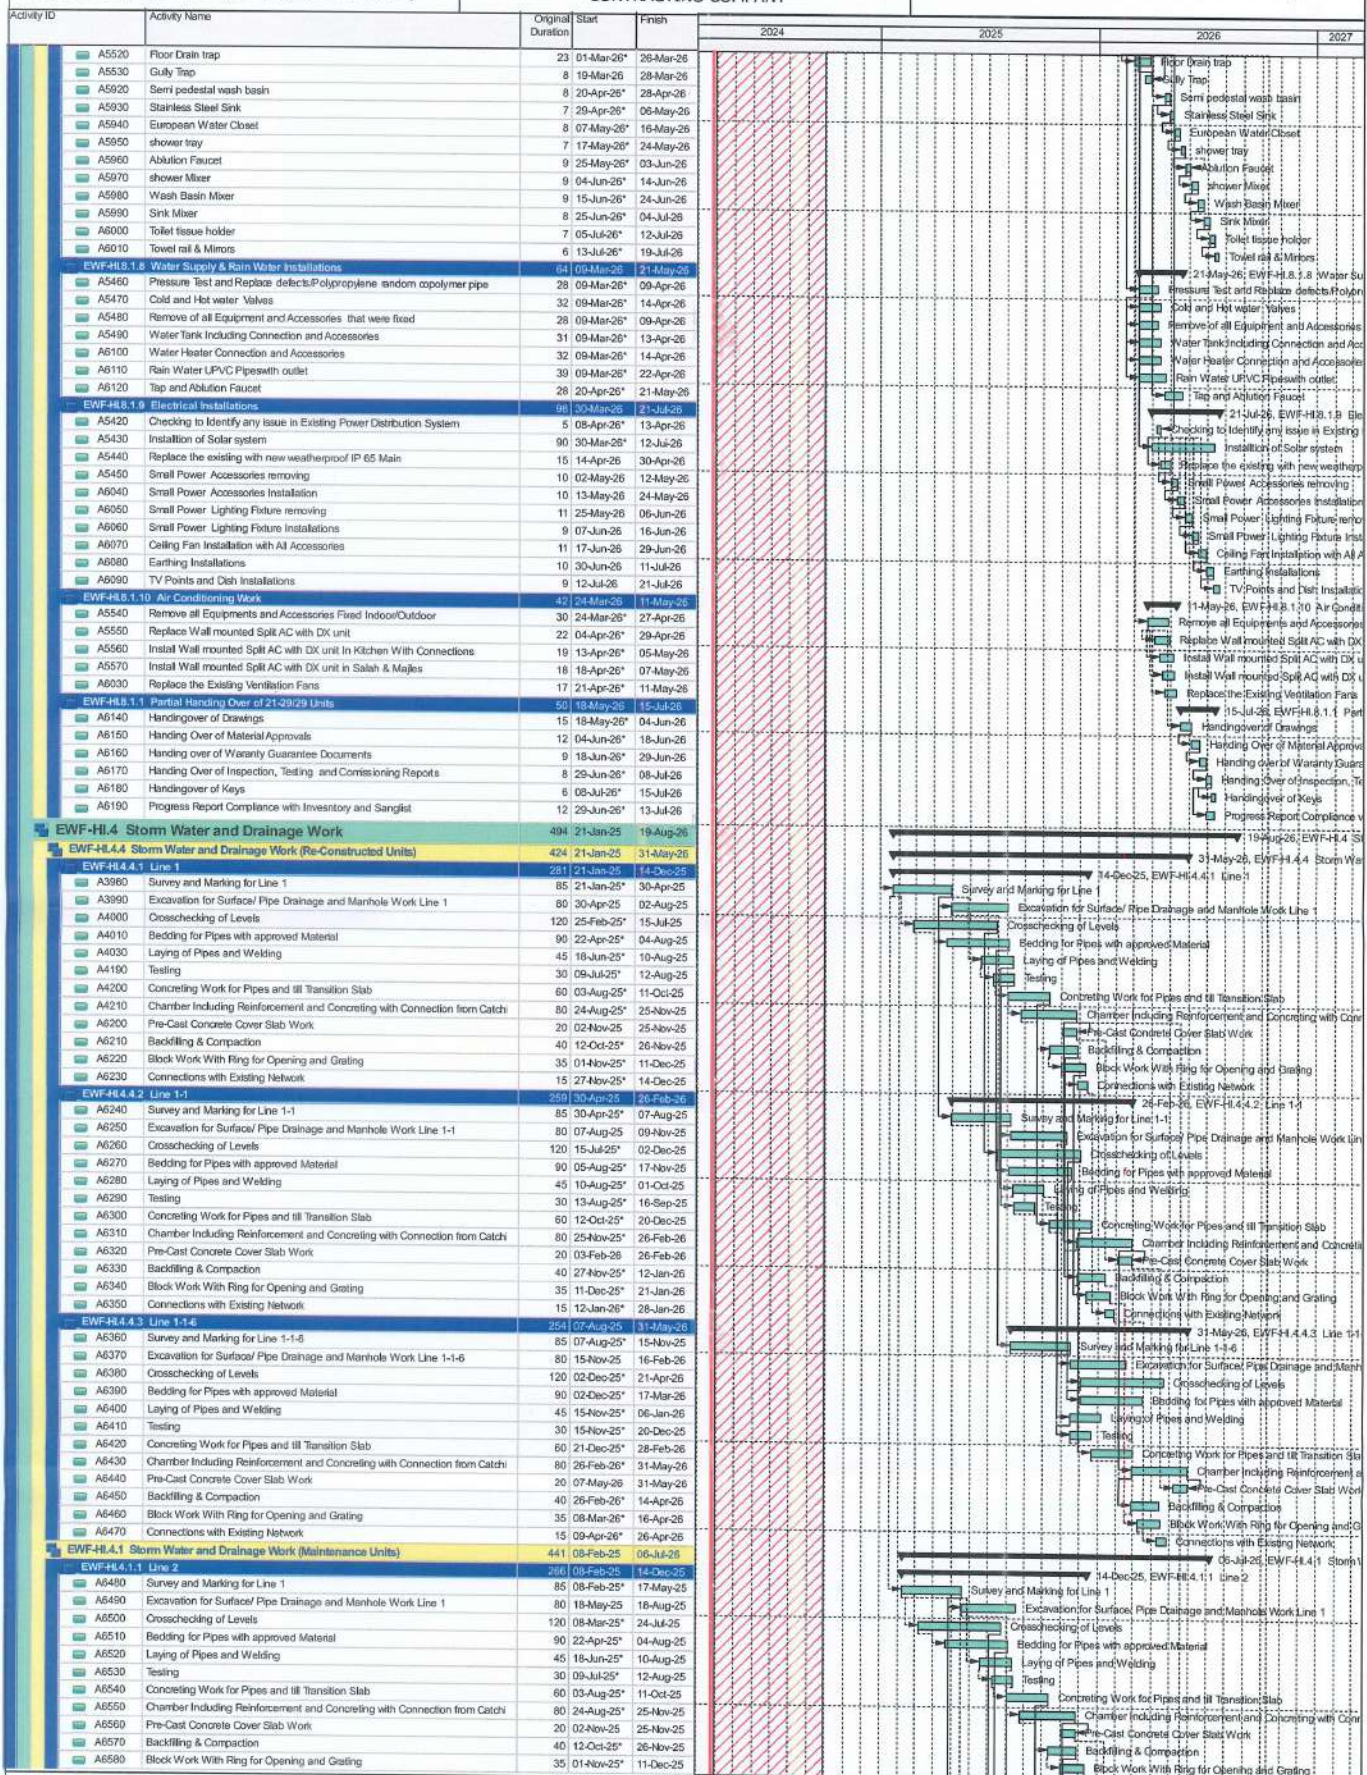


Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work



PROJECT:
CONSTRUCTION, COMPLETION AND MAINTENANCE OF
(20NOS) HOUSING UNITS AND MAINTENANCE OF
(32NOS) HOUSING UNITS AT HALANIYAT ISLAND IN
DHOVAR GOVERNORATE (TENDER NO : 213/2023)

CLIENT: MINISTRY OF HOUSING AND URBAN PLANNING
CONSULTANT: AL MANARAH ENGINEERING
CONSULTANCY
CONTRACTOR: EAST WATERFALLS TRADING &
CONTRACTING COMPANY

MOBILIZATION: 03 JUNE 2024 TO 30 SEPT. 2024
PROJECT DURATION: 730 Days
PROJECT COMMENCEMENT DATE: 01st Oct, 2024
PROJECT COMPLETION DATE: 30th Sep, 2026

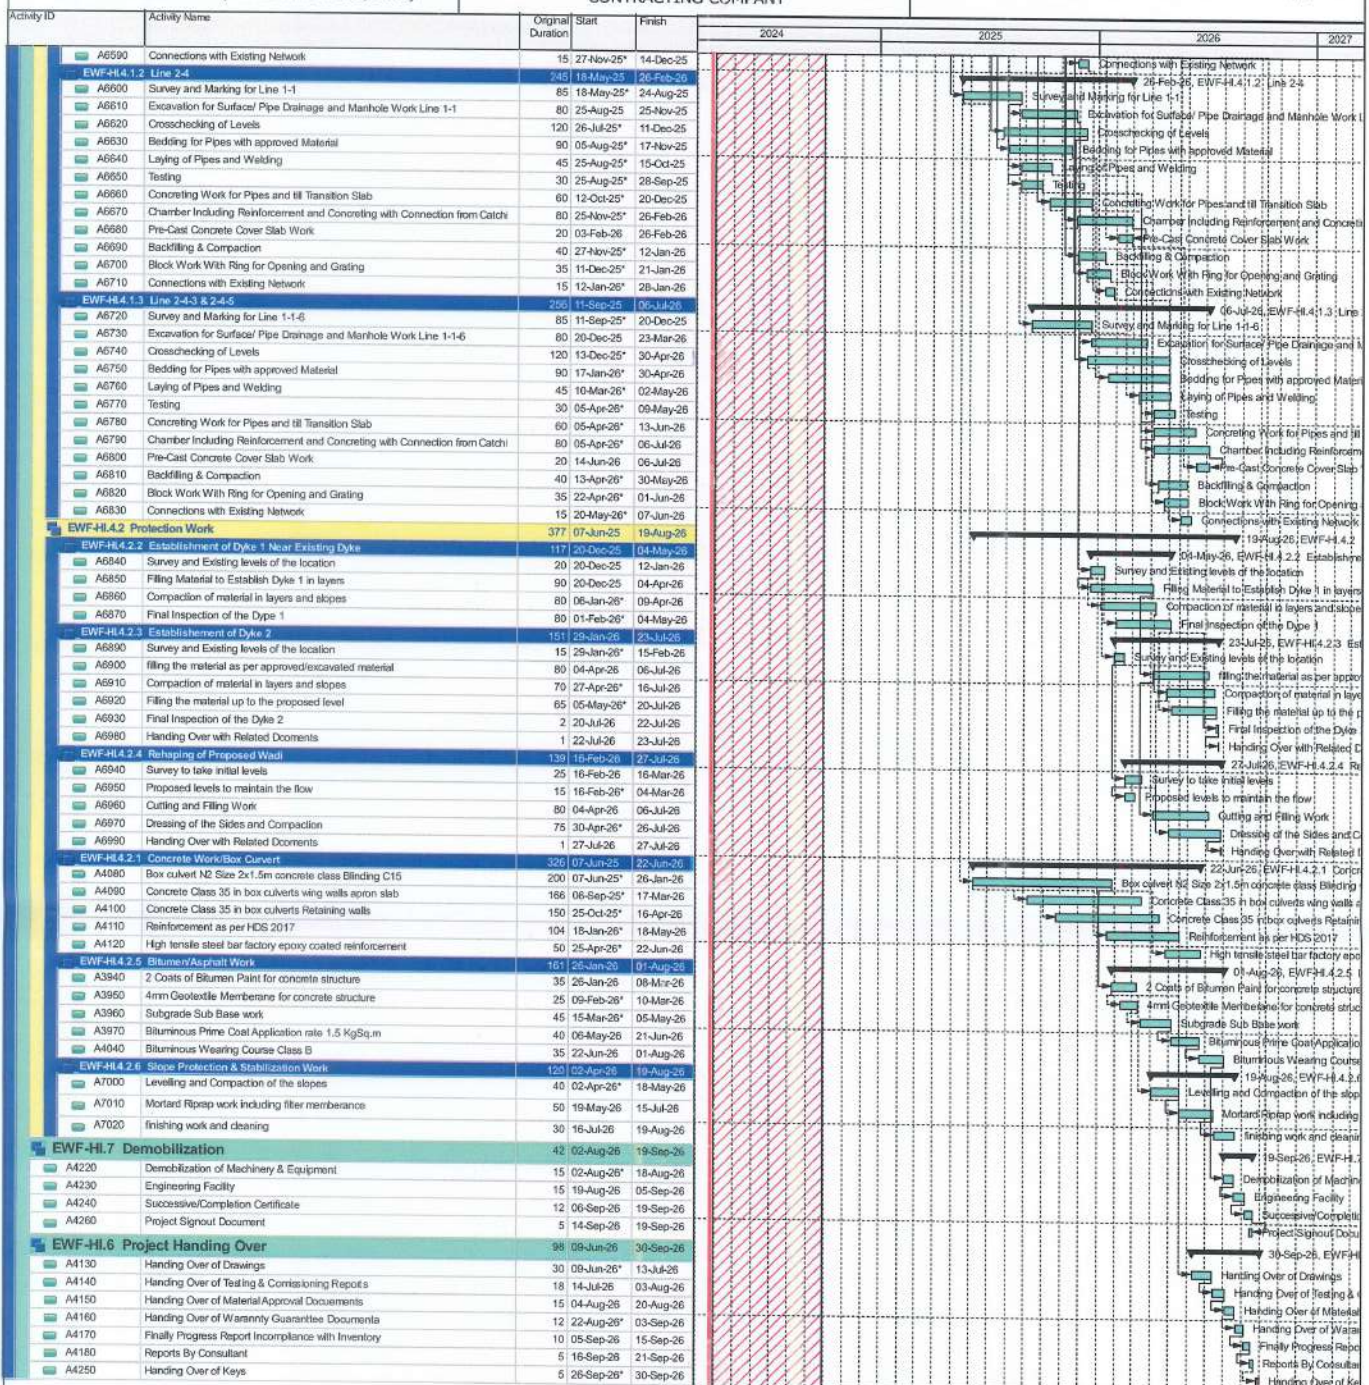

Actual Level of Effort Remaining Work
Actual Work Critical Remaining Work

Muhammad Ahmed

